










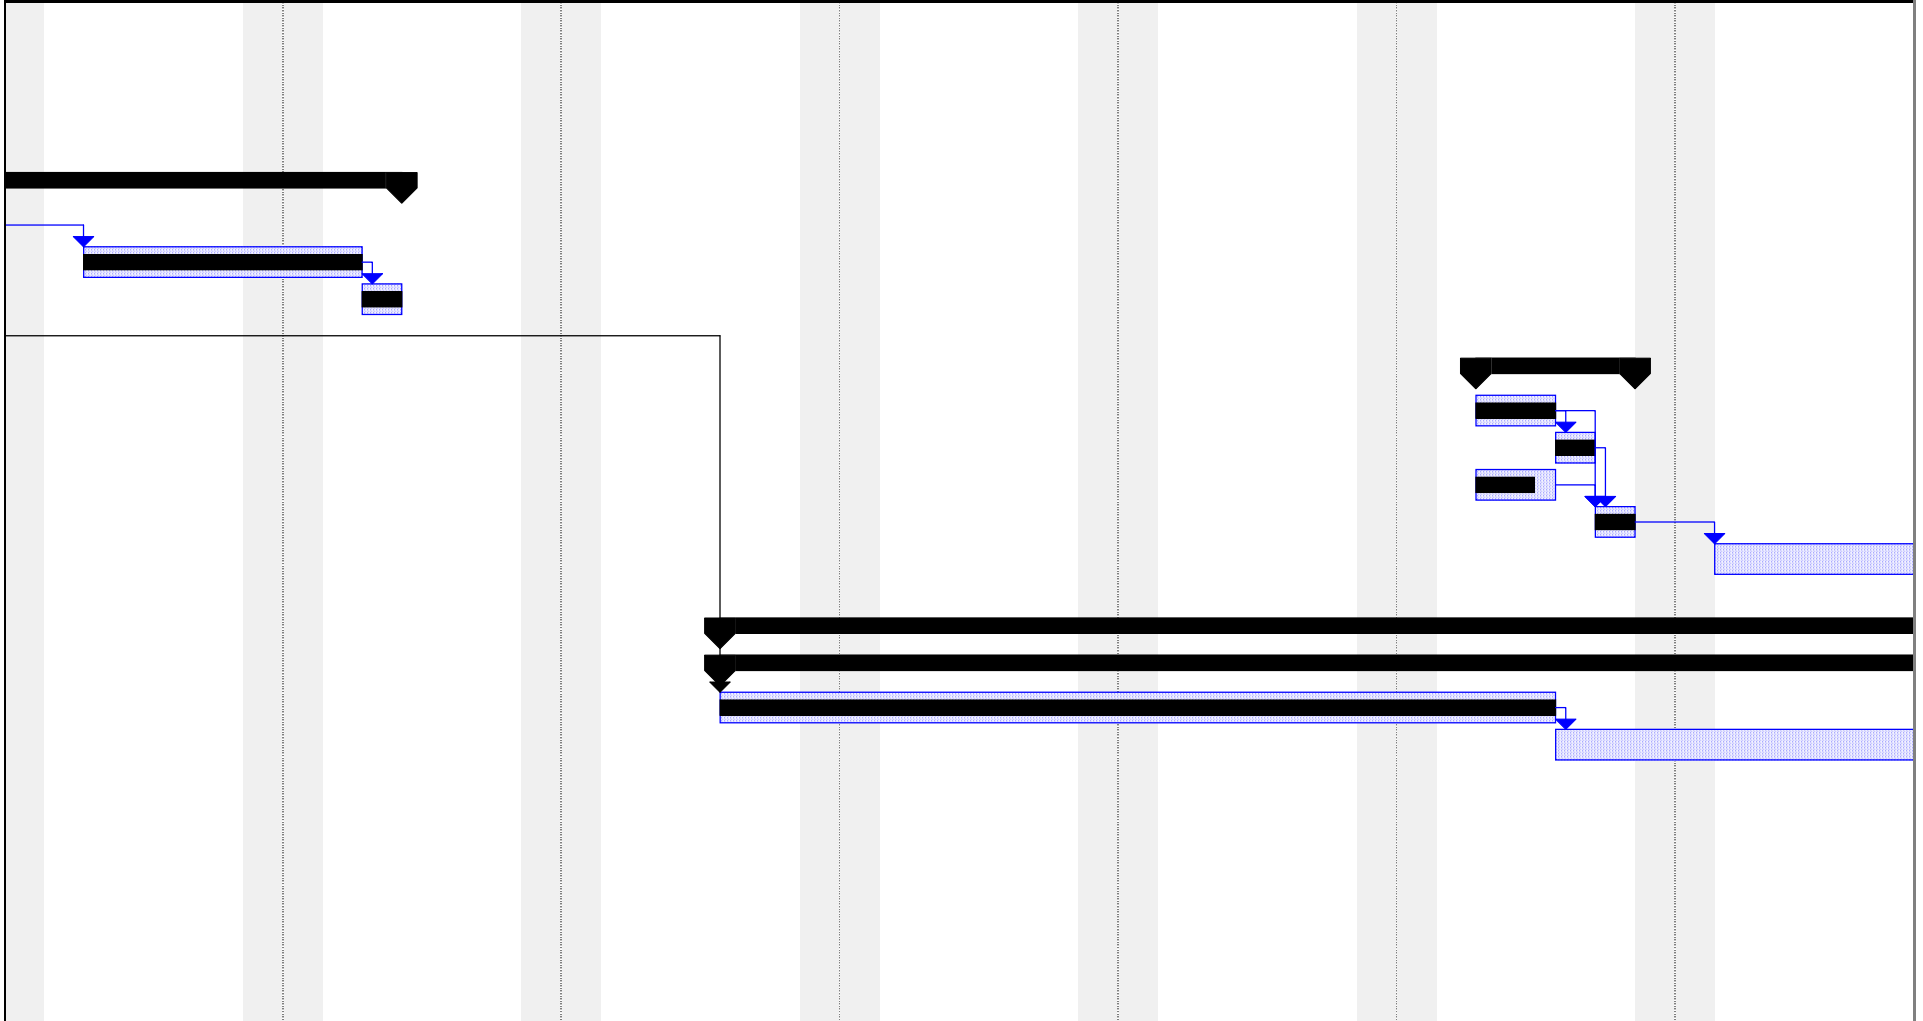
ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Jul 22,			
							F	S	S	M
1	<b>Campus Firewall Upgrade</b>	<b>236 days?</b>	<b>Mon 7/23/07</b>	<b>Mon 6/16/08</b>						
2	<b>Phase 1 Upgrades</b>	<b>45 days?</b>	<b>Mon 7/23/07</b>	<b>Fri 9/21/07</b>						
3	Procure Phase 1 firewalls	1 day?	Mon 7/23/07	Mon 7/23/07						
4	deploy 30 515R and 515UR sites	30 days	Mon 8/6/07	Fri 9/14/07						
5	Trade-in 30 firewalls with cisco	5 days	Mon 9/17/07	Fri 9/21/07	4					
6	<b>Analysis of remaining sites</b>	<b>32 days?</b>	<b>Mon 9/24/07</b>	<b>Tue 11/6/07</b>						
7	master list of campuses	10 days	Mon 9/24/07	Fri 10/5/07	5					
8	Analyse High/Low volume sites	5 days	Tue 10/30/07	Mon 11/5/07	7					
9	Identify models for each site	1 day?	Tue 11/6/07	Tue 11/6/07	8					
10	Complete list of firewalls needed	1 day?	Mon 7/23/07	Mon 7/23/07						
11	<b>Analyse Switch configuration</b>	<b>4 days?</b>	<b>Tue 12/4/07</b>	<b>Fri 12/7/07</b>		<b>Design Engineer</b>				
12	HWIC testing	2 days	Tue 12/4/07	Wed 12/5/07						
13	Decision: HWIC vs 8 port switch	1 day?	Thu 12/6/07	Thu 12/6/07	12					
14	Port count	2 days	Tue 12/4/07	Wed 12/5/07						
15	Define standard Model for config	1 day?	Fri 12/7/07	Fri 12/7/07	12,13,14					
16	Compare each site with model (site Analysis)	15 days	Mon 12/10/07	Fri 12/28/07	15					
17	Complete list of switches/consoles/interfaces	1 day?	Mon 12/31/07	Mon 12/31/07	16					
18	<b>Procurement</b>	<b>63 days</b>	<b>Thu 11/15/07</b>	<b>Mon 2/11/08</b>						
19	<b>Initial procurement</b>	<b>30 days</b>	<b>Thu 11/15/07</b>	<b>Wed 12/26/07</b>						
20	Initial PO processing (14 firewalls)	15 days	Thu 11/15/07	Wed 12/5/07	10					
21	Shipping on initial PO	15 days	Thu 12/6/07	Wed 12/26/07	20					
22	<b>Final procurement</b>	<b>30 days</b>	<b>Tue 1/1/08</b>	<b>Mon 2/11/08</b>						
23	Final PO processing (remaining all equip)	15 days	Tue 1/1/08	Mon 1/21/08	17					
24	shipping on final PO (remaining all equip)	15 days	Tue 1/22/08	Mon 2/11/08	23					
25	<b>Deployment</b>	<b>120 days</b>	<b>Tue 1/1/08</b>	<b>Mon 6/16/08</b>						
26	Scheduling with campuses	15 days	Tue 1/1/08	Mon 1/21/08	17					
27	68 Upgrades (3 per week)	115 days	Tue 1/8/08	Mon 6/16/08	26SS+5 days					
28	Complete Firewall and Switch Deployment	1 day?	Tue 6/17/08	Tue 6/17/08	27					

Project: MSProj11 Date: Thu 1/31/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	






Oct 28, '07					Nov 4, '07					Nov 11, '07					Nov 18, '07					Nov 25, '07					Dec 2, '07					Dec 9, '07																		
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S




Project: MSProj11  
Date: Thu 1/31/08

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

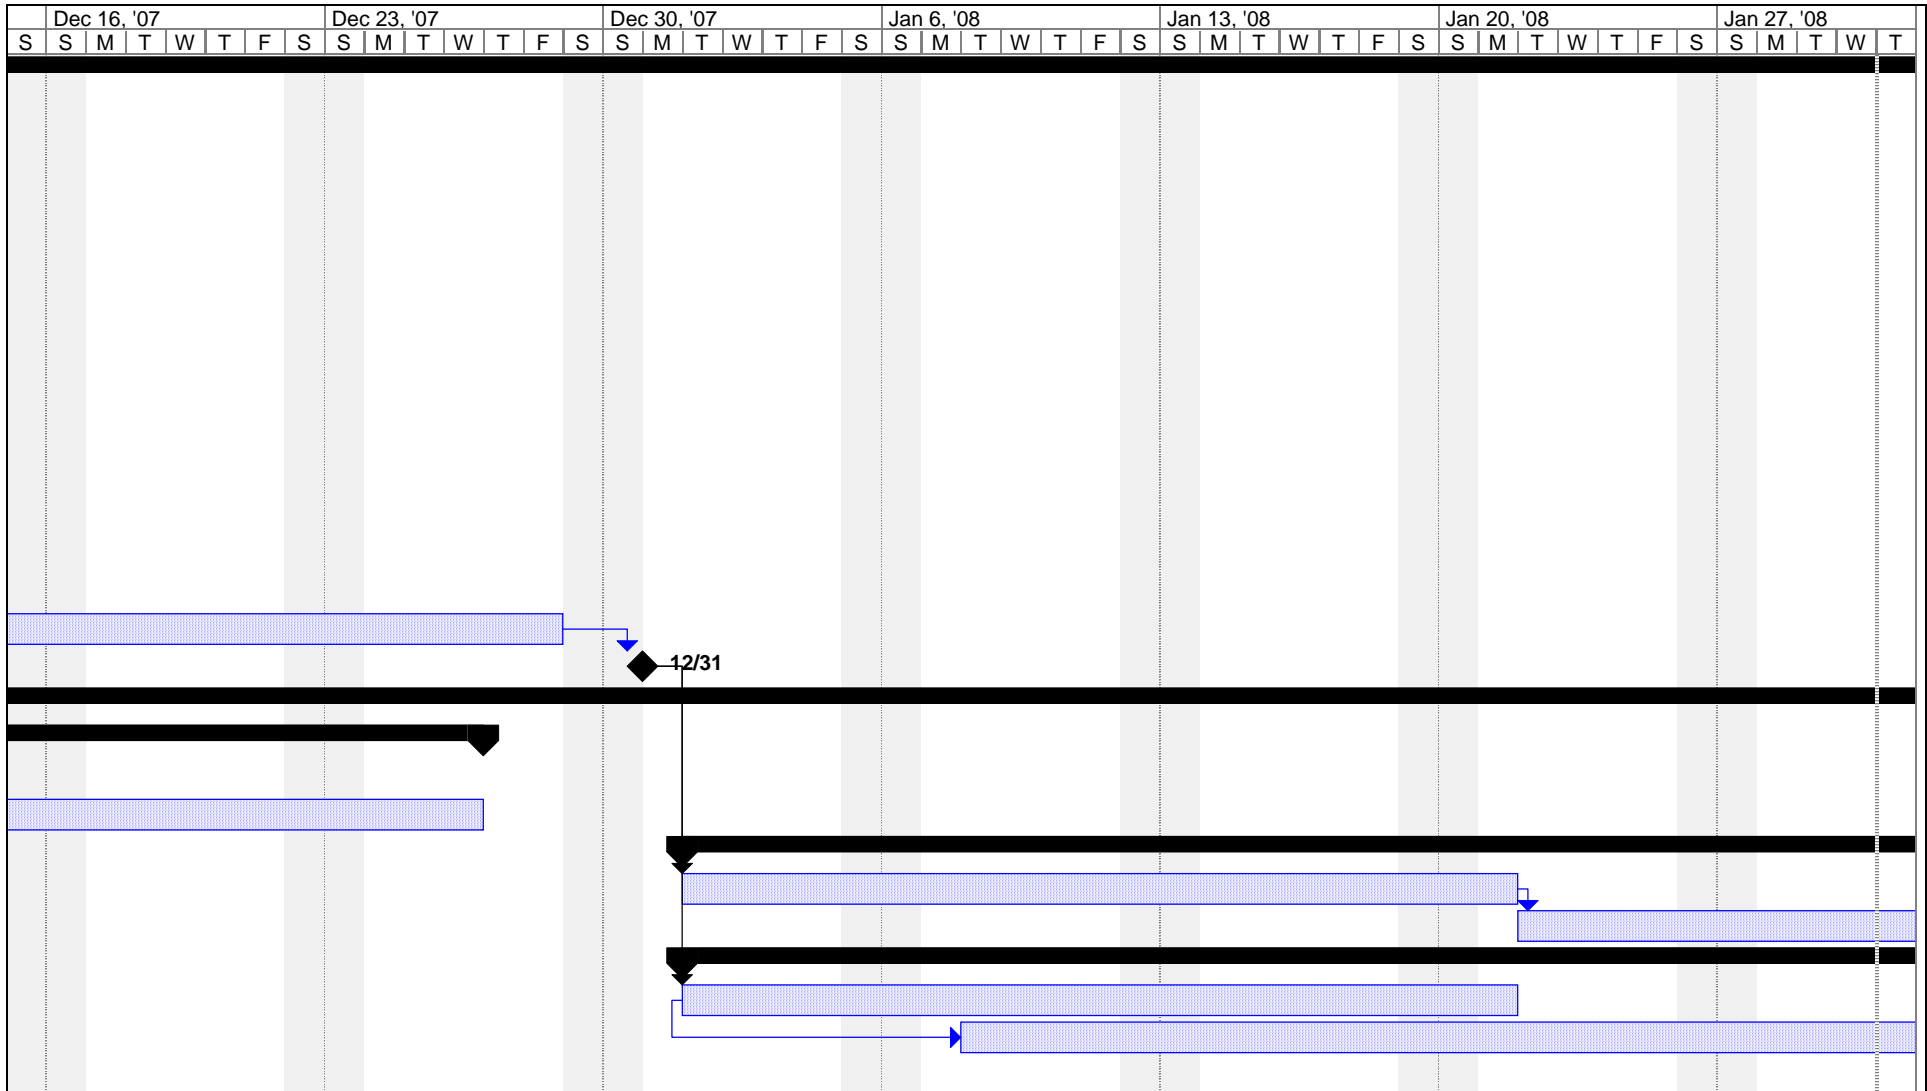

Project: MSProj11  
Date: Thu 1/31/08


Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

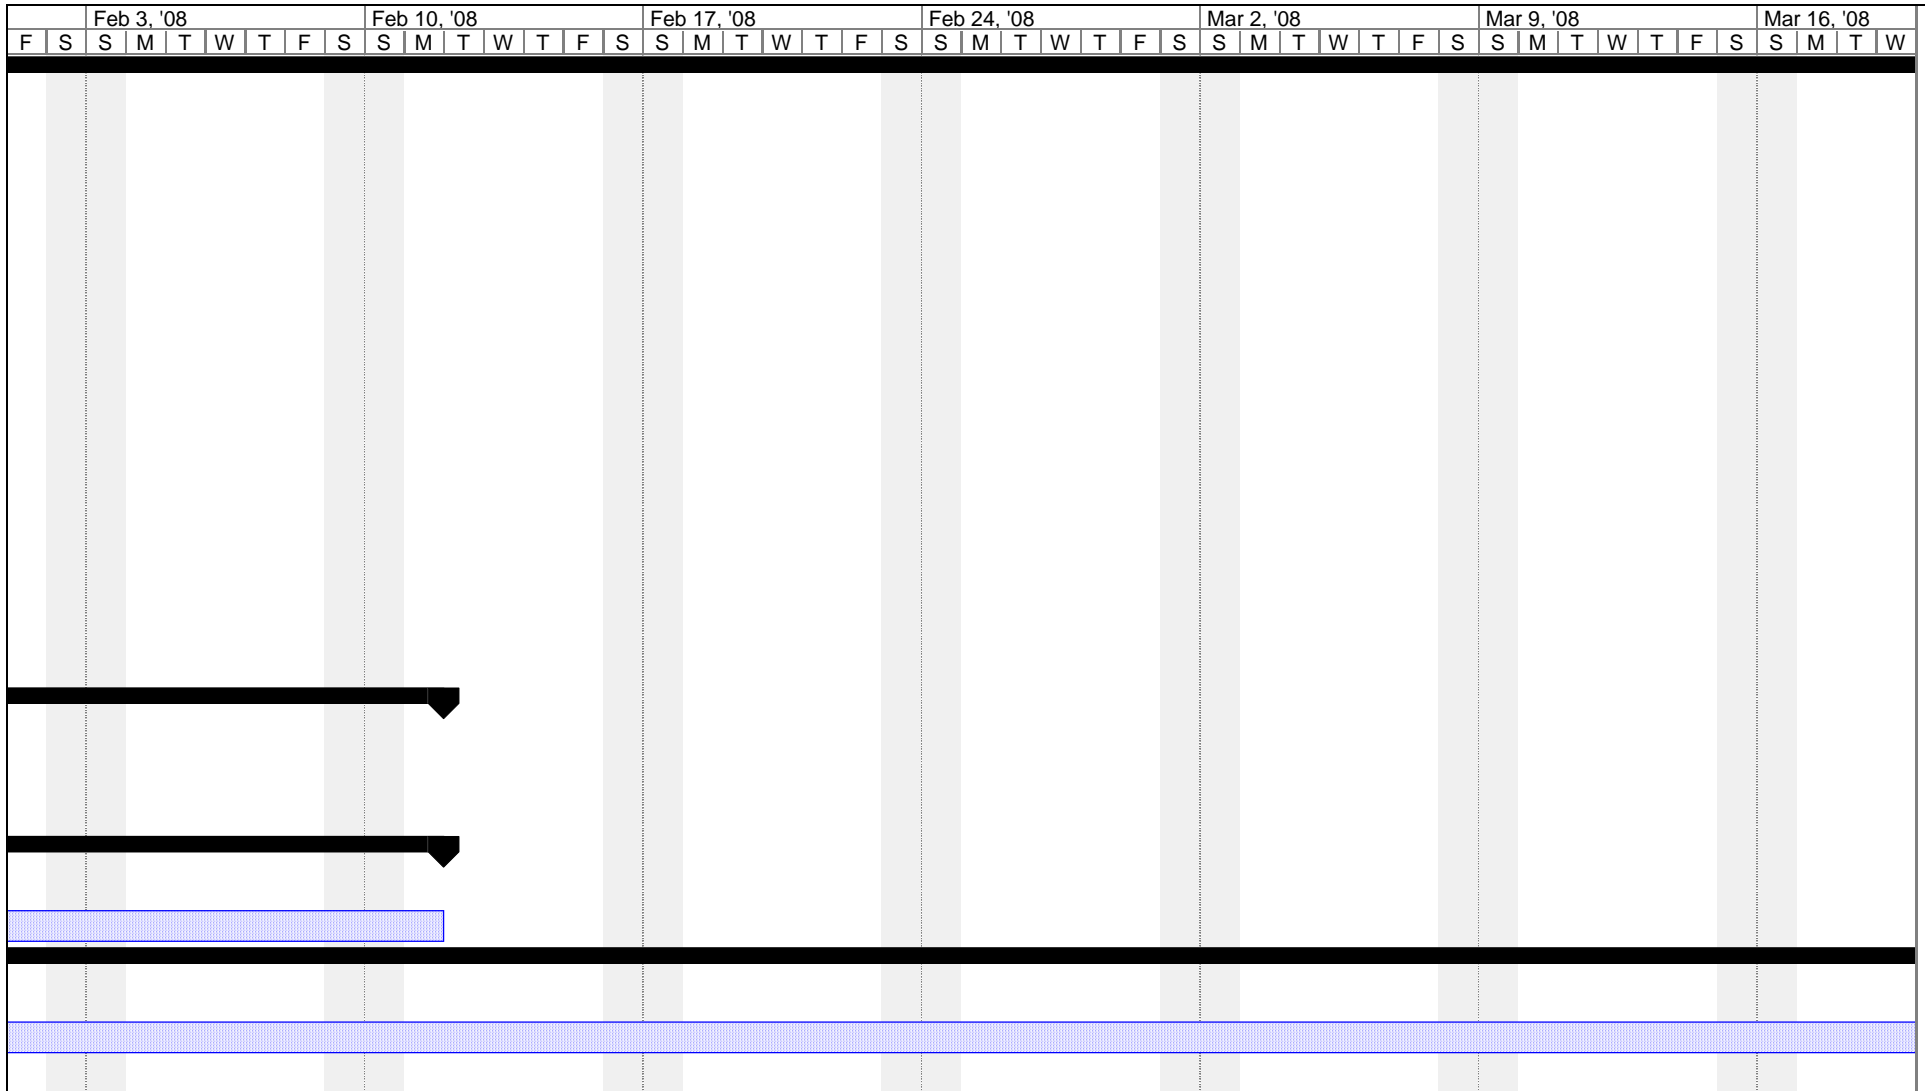

Project: MSProj11  
Date: Thu 1/31/08

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



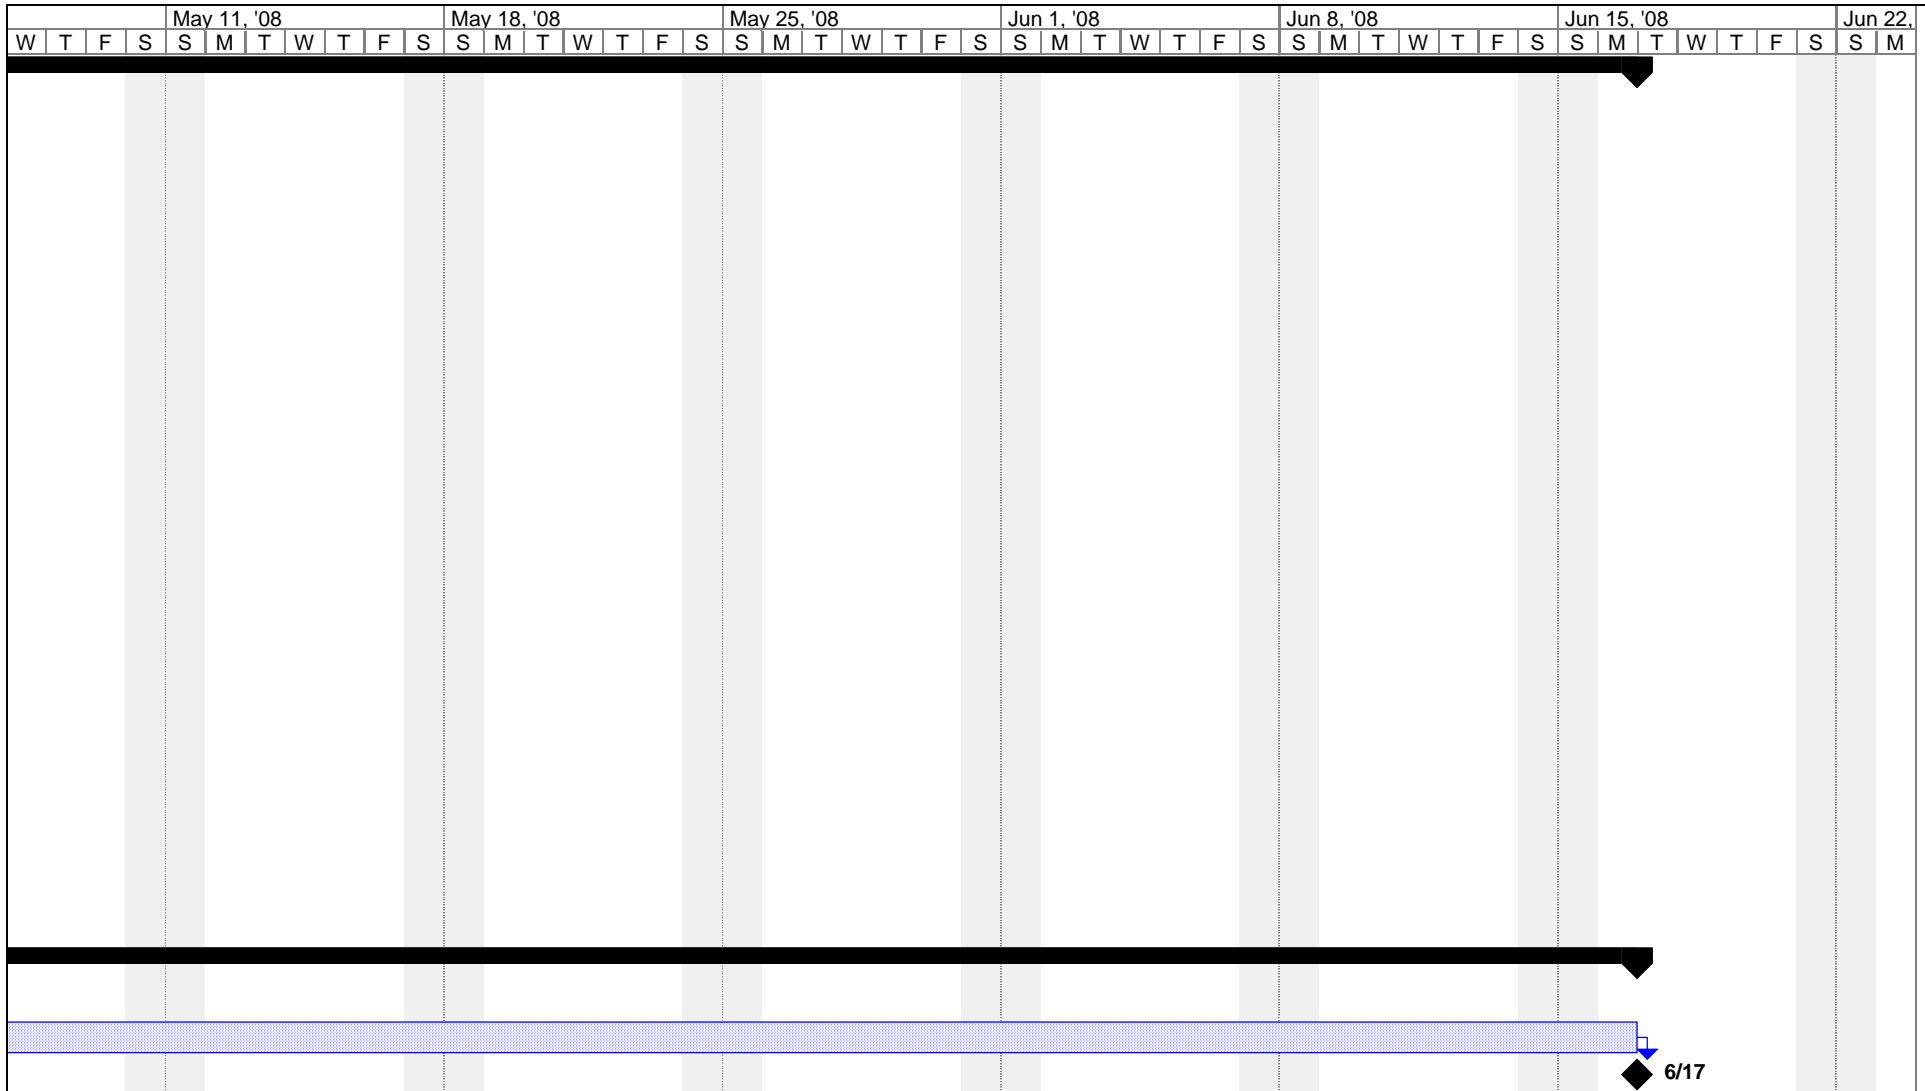

Project: MSProj11  
Date: Thu 1/31/08

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
